



# **CRA BOARD MEETING**

**Construction Work  
FOR A1A COMPLETE STREETS AND UNDERGROUNDING  
OF OVERHEAD UTILITIES  
Hollywood Boulevard to Sheridan Street  
February 2, 2022**

# SR A1A Prior to FDOT RRR



**SR A1A as of December 2016 – Looking North**



# SR A1A Current Conditions





# CRA Complete Streets/Undergrounding



**Proposed Improvements**

# Geographical Area and Scope of work



- ☐ Undergrounding of overhead utilities (FPL, Comcast, AT&T, Hotwire, Crown Castle, others)
- ☐ Landscaping along both sidewalks and medians
- ☐ Pedestrian lighting both sidewalks
- ☐ Decorative pavement on the west side of A1A to match east side of A1A
- ☐ New traffic signal at Garfield Street with pavement marking and signage
- ☐ 3 Conduits for future traffic signals (Nebraska, Carolina, Scott)



# Complete Street Construction Mobilization



- ❑ October 6, 2021: Board Approval of GMP
- ❑ October 21, 2021: Executed Contract
- ❑ November 17, 2021: Issuance of Notice to Proceed, effective January 17, 2022.
- ❑ October 26, 2021: Issuance of Payment and Performance Bond
- ❑ November 2021: Shop Drawing review for long lead item material purchase
  - ❑ November 2021: City Permit Approval Review Process
  - ❑ December 6, 2021: Coffee with the Crew at Nebraska Street Parking Garage
  - ❑ January 17, 2022- Mobilization
  - ❑ January 18, 2022- Utility Markings
  - ❑ January 20, 2022- Soft digging (exploratory digging) to collect below ground infrastructure information

# General Contractor's Team

## **BURKHARDT CONSTRUCTION INC.** **General Contractors**

### **Sub Contractors:**

#### **Viking/Danella**

Undergrounding of Utilities

#### **Gerelco**

Lighting and Signalization

#### **Arazoza Brothers Corporation**

Landscape and Irrigation

#### **David Wayne Hardscapes, LLC**

Paver Installation

# Coffee with the Crew/ Public Outreach Program



- ☐ Bi-Weekly e-mail blast with project updates.
- ☐ Bi- Weekly CRA website update
- ☐ Monthly “Coffee with the Crew” – Next Coffee meeting scheduled for Feb 17




- ☐ Phone contact 24/7 : (561) 659-1400
- ☐ Coordination with HBBA and HBCA
- ☐ Lane closures coordination with FDOT, Residents and Business owners





# Construction Sequence North to South

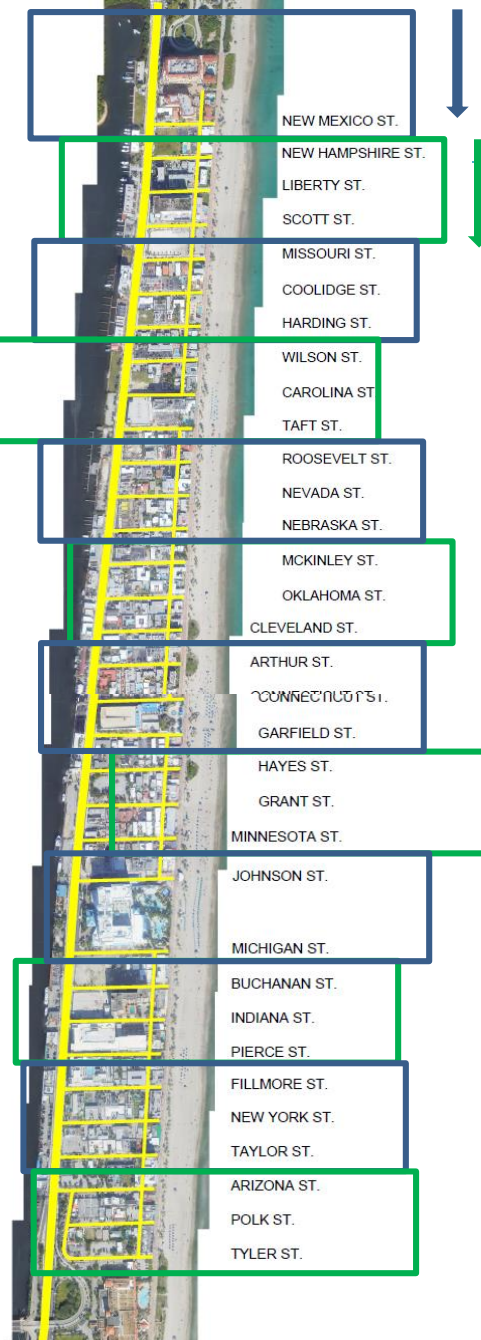

NEW MEXICO ST.  
NEW HAMPSHIRE ST.  
LIBERTY ST.  
SCOTT ST.  
MISSOURI ST.  
COOLIDGE ST.  
HARDING ST.  
WILSON ST.  
CAROLINA ST.  
TAFT ST.  
ROOSEVELT ST.  
NEVADA ST.  
NEBRASKA ST.  
MCKINLEY ST.  
OKLAHOMA ST.  
CLEVELAND ST.  
ARTHUR ST.  
CONNORS ST.  
GARFIELD ST.  
HAYES ST.  
GRANT ST.  
MINNESOTA ST.  
JOHNSON ST.  
MICHIGAN ST.  
BUCHANAN ST.  
INDIANA ST.  
PIERCE ST.  
FILLMORE ST.  
NEW YORK ST.  
TAYLOR ST.  
ARIZONA ST.  
POLK ST.  
TYLER ST.

## ACTIVITIES TO MINIMIZE IMPACT TO RESIDENTS/ BUSINESS OWNERS:

- ☐ Close small sections of lanes in each direction at a time.
- ☐ Restore sidewalk to safe walkable condition at end of every workday.
- ☐ Ensure access to driveways, coordinate parking areas impacts w/ property owner.
- ☐ The lane closures will only impact 2-3 blocks at a time and construction sequence to be north to south.
- ☐ One or more subcontractors may be working concurrently.
- ☐ Sheridan Street bridge project/closures coordination with FDOT project manager and GC.

# 30-60-90 Look Ahead



**30**  
Day

- ☐ Exploratory digging
- ☐ Installation of franchise utility conduits along the west side of A1A- starting on Sheridan Street North due South

**60**  
Day


- ☐ Installation of franchise utility conduits along west side of A1A

**90**  
Day

- ☐ Installation of franchise utility conduits along the west side of A1A
- ☐ All above dates are contingent to site conditions and exploratory results



# Project Cost:

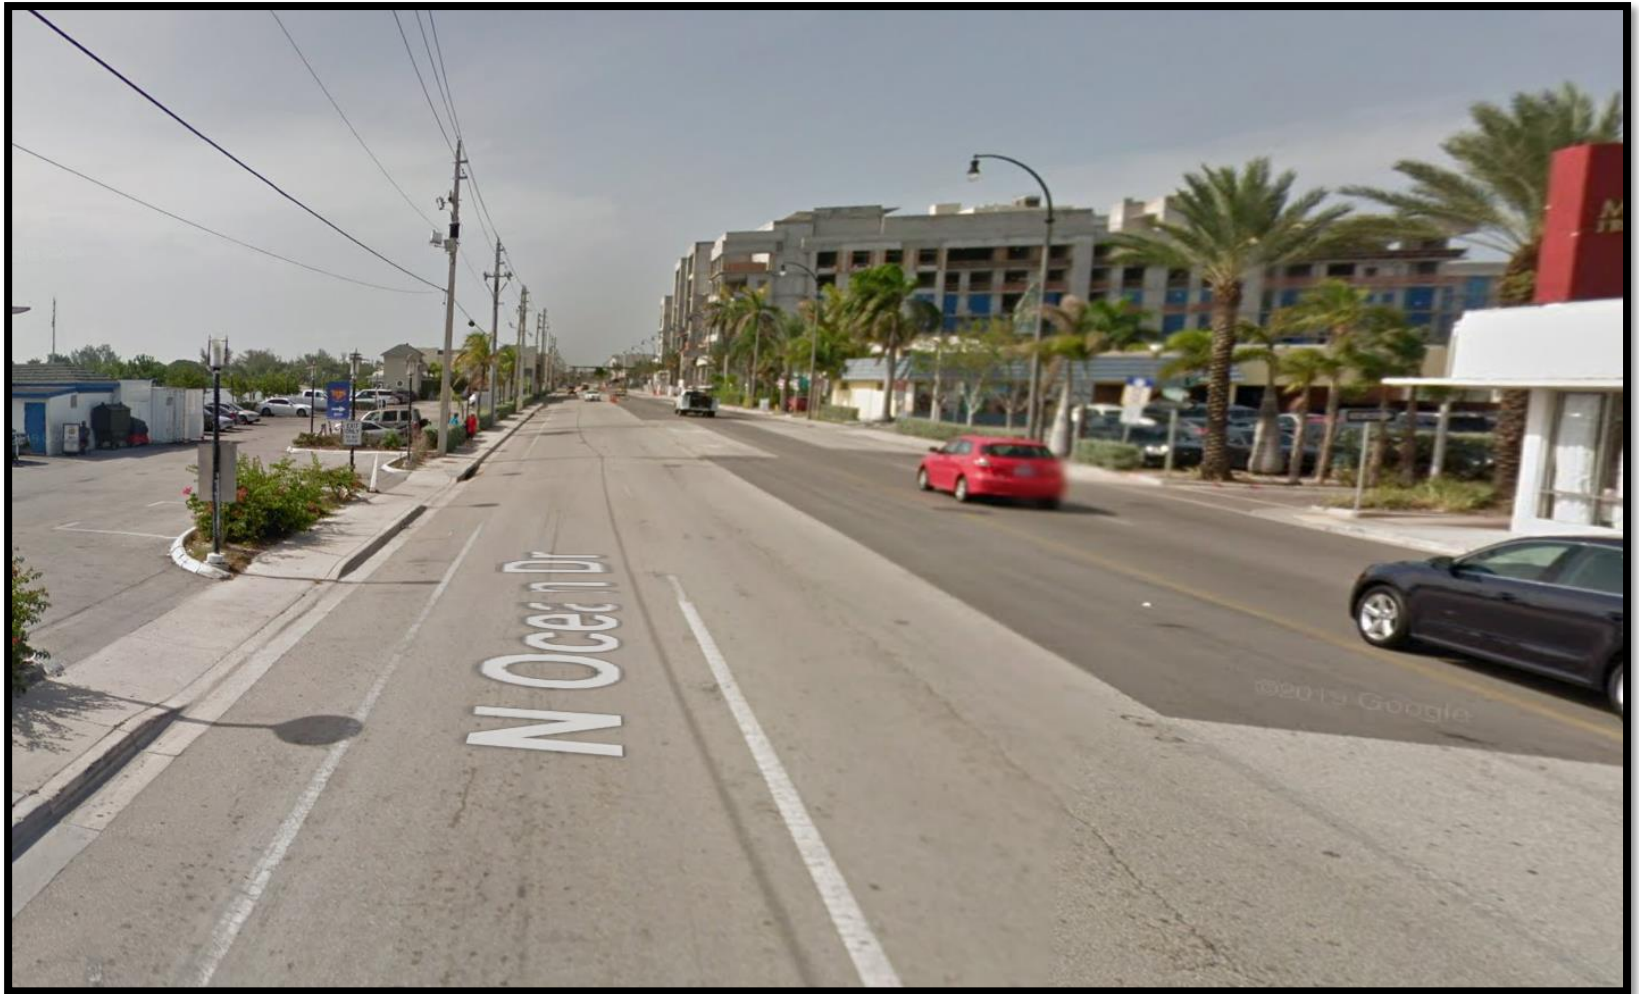

# Project Overview





# Project Scope of Work and Timeline

TIMELINE - COMMUNITY REDEVELOPMANT AGENCY CAPITAL PROJECTS																																																		
						FY 2022								FY 2023								FY 2024																												
PROJECT TIMELINE	May-21	Jun-21	Jul-21	Aug-21	Sep-21	Oct-21	Nov-21	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22	Aug-22	Sep-22	Oct-22	Nov-22	Dec-22	Jan-23	Feb-23	Mar-23	Apr-23	May-23	Jun-23	Jul-23	Aug-23	Sep-23	Oct-23	Nov-23	Dec-23	Jan-24	Feb-24	Mar-24	Apr-24	May-24	Jun-24	Jul-24	Aug-24	Sep-24	Oct-24								
A1A Complete Streets & Undergrounding of Overhead Utilities	Bidding and GMP Negotiation					Reso and Board Approval	Contract execution Bonds	Construction Activities								FPL Hookup								Project Closeout																										

- ☐ Undergrounding of overhead utilities (FPL, Comcast, AT&T, Hotwire, Crown Castle, others)
- ☐ Landscaping along both sidewalks and medians
- ☐ Pedestrian lighting both sidewalks
- ☐ Decorative pavement on the west side of A1A to match east side of A1A
- ☐ New traffic signal at Garfield Street with pavement marking and signage. (Nebraska, Carolina, Scott)
- ☐ Maintenance of Traffic ( MOT)
- ☐ Community Outreach

**QUESTIONS?**
